WEEK 43 · 20–24 OCTOBER 2026

Orders platform

Reads are under their latency budget for the first full week. The move to queued order events is a week behind, because billing's consumer needs a second review.

OVERALL	P99 LATENCY	CACHE HITS	ORDERS A DAY
At risk	**166 ms**	**91 %**	**18 420**
2 of 4 milestones done	−16 ms on last week · target 200 ms	−3 % on last week · target 95 %	+1 320 on last week

Highlights

- The cache warms in 40 seconds after a deploy, down from 6 minutes.
- Email reads order events from the queue; the polled table serves billing and analytics only.

Risks

Risk	Severity	Owner	Mitigation
Billing's consumer is reviewed late	**High**	Billing lead	Pair on the review on Monday
Cache hit rate keeps falling	Medium	Platform	Find which keys miss

Milestones

Done	**Cache in front of order reads**	10 Oct
Done	**Email on the queue**	24 Oct
At risk	**Billing on the queue** a week behind; review moved to Monday	31 Oct
On track	**Polled table retired**	14 Nov

Figure 1: 4 milestones: 2 done, 1 on track, 1 at risk.

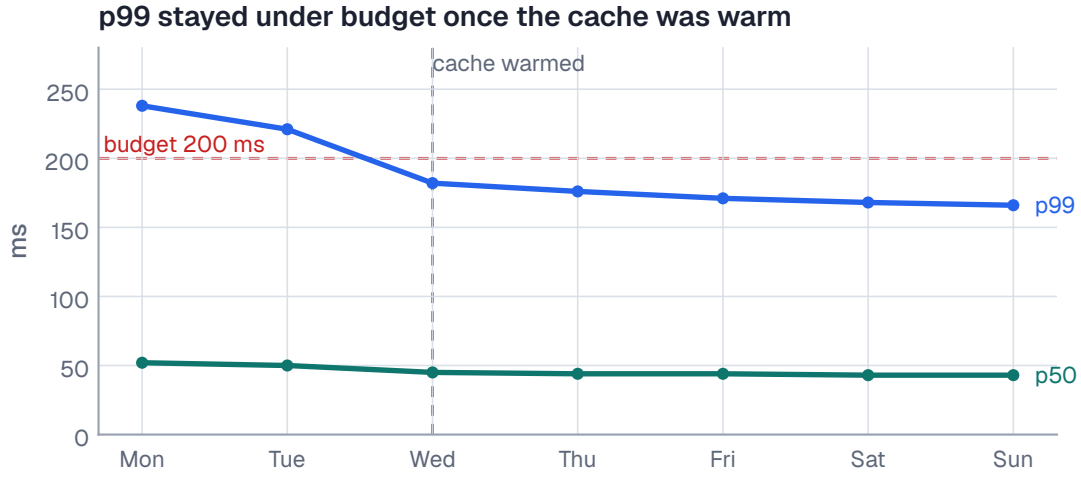

Figure 2: p99 fell under its budget on Wednesday, when the cache had warmed.

Needed from you

1. Agree that analytics may keep its own copy of events (decision by Friday).
2. Lend one billing engineer for Monday's review.
